



Sri Lanka Institute of Information Technology
Software Quality Assurance IT4100

25-26J-177

Student Name	Student Id
Jayaweera R C	IT22215574
Sumanaweera A D H R	IT22283344
Jayaweera J P S P	IT22277572
Kaushan M K	IT22569622


Table of Contents

Board Overview	3
Grid View of the MS Planner	5
Progress Monitoring	6
Schedule View.....	7
Tasks by Member	8
References	10

Board Overview

Planner Board Overview

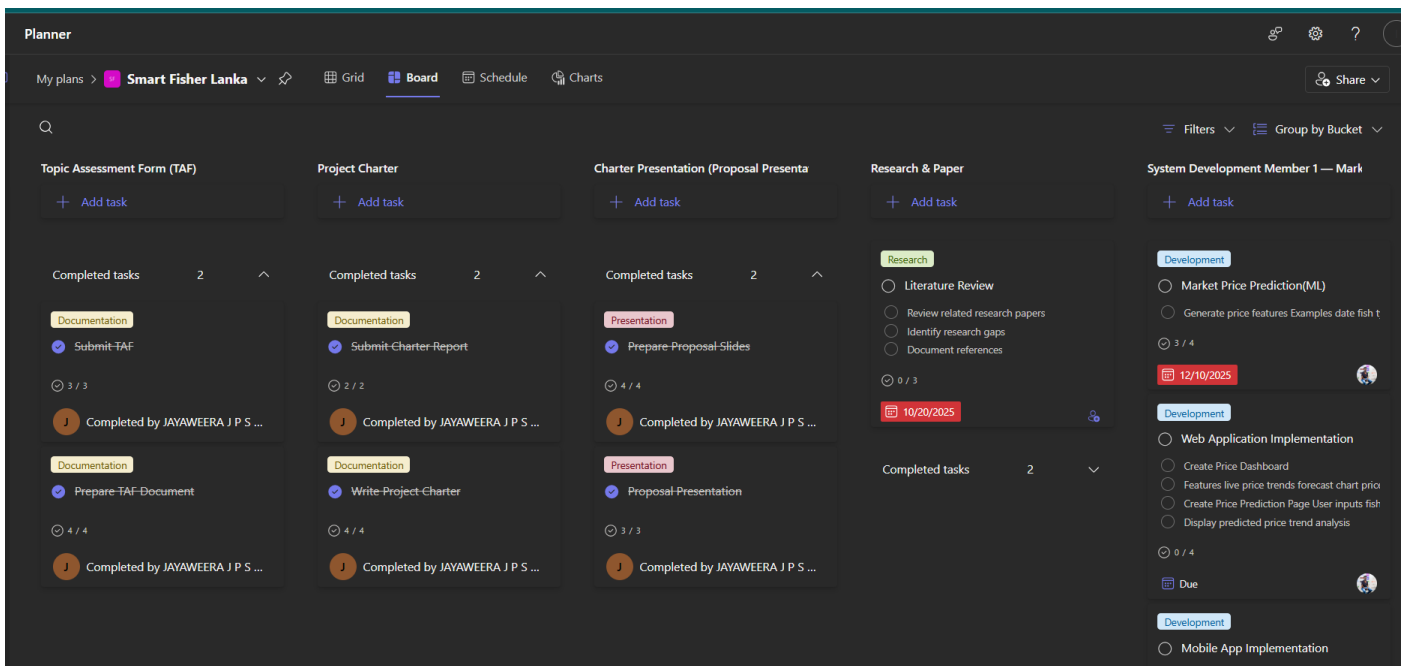- Initialization
- Requirement Analysis
- Charter Report
- System Development
- System Integration
- System Testing
- PP1
- PP2



The screenshot displays a 'Planner' application interface with a Kanban board. The board is organized into five columns, each representing a different project phase or task category. Each column has a header with a search icon, a '+ Add task' button, and a 'Completed tasks' count. Below the header, tasks are listed with their status (e.g., 'Submitted', 'Prepared', 'Completed') and assigned users (e.g., 'JAYAWEERA J P S ...').

- Topic Assessment Form (TAF):** 2 completed tasks. Tasks include 'Submit-TAF' and 'Prepare-TAF-Document'.
- Project Charter:** 2 completed tasks. Tasks include 'Submit-Charter-Report' and 'Write-Project-Charter'.
- Charter Presentation (Proposal Presentation):** 2 completed tasks. Tasks include 'Prepare-Proposal-Slides' and 'Proposal-Presentation'.
- Research & Paper:** 0/3 tasks. Tasks include 'Literature Review', 'Review related research papers', 'Identify research gaps', and 'Document references'.
- System Development Member 1 — Mark:** 0/4 tasks. Tasks include 'Market Price Prediction(ML)', 'Generate price features Examples date fish t', 'Web Application Implementation', 'Create Price Dashboard', 'Features live price trends forecast chart prio', 'Create Price Prediction Page User inputs fish', and 'Display predicted price trend analysis'.

My plans > **Smart Fisher Lanka** **Board**

Filters

Unassigned

+ Add task

Testing

☐ Fish Quality Grading Testings

System Testing

Testing

☐ Fish Zone Prediction Testings

System Testing

Testing

☐ Fish Quality Grading Testings

System Testing

Testing

☐ DATCIE Trip Cost Engine Testings

System Testing

JAYAWEERA J P S P it22277572

+ Add task

Development

☐ Trip Data Processing

System Development :Member 4 — DATCIE Tr...

☐ Prepare boat trip dataset

☐ Process fuel usage data

0 / 2

Due

Development

☐ Trip Cost Calculation

System Development :Member 4 — DATCIE Tr...

☐ Implement profit calculation

1 / 2

Due

Development

☐ Backend API (NestJS)

JAYAWEERA R C it22215574

+ Add task

Development

☐ Ocean Data Processing

System Development :Member 2 — Fish Zone...

☐ Prepare ocean condition dataset

☐ Process spatial coordinates

0 / 2

12/10/2025

Development

☐ Fishing Zone Prediction

System Development :Member 2 — Fish Zone...

☐ Implement zone prediction logic

☐ Identify fishing hotspots

0 / 2

12/20/2025

Development

KAUSHAN M K it22569622

+ Add task

Development

☐ Price Data Processing

System Development Member 1 — Market Pri...

☐ Prepare historical price dataset

☐ Clean data

☐ Generate price features

0 / 3

12/10/2025

Development

☐ Price Prediction Implementation

System Development Member 1 — Market Pri...

☐ Implement price prediction function

☐ Generate 31-day forecasts

☐ Detect price trends

0 / 3

12/10/2025

SUMANAWEERA A.D.H.R it22283344

+ Add task

Development

☐ Image Processing

System Development :Member 3 — Fish Quali...

☐ Prepare fish image dataset

☐ Implement fish detection

0 / 2

12/15/2025

Development

☐ Quality Analysis

System Development :Member 3 — Fish Quali...

☐ Implement quality grading

☐ Estimate fish weight

0 / 2

01/25

Development

Filters

Unassigned

+ Add task

Testing

☐ Fish Quality Grading Testings

System Testing

Testing

☐ Fish Zone Prediction Testings

System Testing

Testing

☐ Fish Quality Grading Testings

System Testing

Testing

☐ DATCIE Trip Cost Engine Testings

System Testing

JAYAWEERA J P S P it22277572

+ Add task

Development

☐ Trip Data Processing

System Development :Member 4 — DATCIE Tr...

☐ Prepare boat trip dataset

☐ Process fuel usage data

0 / 2

Due

Development

☐ Trip Cost Calculation

System Development :Member 4 — DATCIE Tr...

☐ Implement profit calculation

1 / 2

Due

Development

☐ Backend API (NestJS)

JAYAWEERA R C it22215574

+ Add task

☐ Prepare ocean condition dataset

☐ Process spatial coordinates

0 / 2

12/10/2025

Development

☐ Fishing Zone Prediction

System Development :Member 2 — Fish Zone...

☐ Implement zone prediction logic

☐ Identify fishing hotspots

0 / 2

12/20/2025

Development

☐ Backend API (NestJS)

System Development :Member 2 — Fish Zone...

☐ Return probability for a location.

☐ Return map heatmap data.

KAUSHAN M K it22569622

+ Add task

Development

☐ Price Data Processing

System Development Member 1 — Market Pri...

☐ Prepare historical price dataset

☐ Clean data

☐ Generate price features

0 / 3

12/10/2025

Development

☐ Price Prediction Implementation

System Development Member 1 — Market Pri...

☐ Implement price prediction function

☐ Generate 31-day forecasts

☐ Detect price trends

0 / 3

12/10/2025

SUMANAWEERA A.D.H.R it22283344

+ Add task

Development

☐ Image Processing

System Development :Member 3 — Fish Quali...

☐ Prepare fish image dataset

☐ Implement fish detection

0 / 2

12/15/2025

Development

☐ Quality Analysis

System Development :Member 3 — Fish Quali...

☐ Implement quality grading

☐ Estimate fish weight

0 / 2

01/25

Development

Grid View of the MS Planner

My plans > **Smart Fisher Lanka**  **Grid**     Share

Q  Filters

Task Name	Assignment	Start date	Due date	Bucket	Progress	Priority	Labels	Quick look
✓ Create Microsoft Planner				Initialization	✓ Completed	Medium	Add label	3/3
✓ Create Git Repository				Initialization	✓ Completed	Medium	Add label	4/4
✓ Create MS Planner & task distribution				Initialization	✓ Completed	Medium	Add label	3/3
✓ Show implemented modules				Progress Presenta	✓ Completed	Medium	Presentation ✕	
✓ Present system architecture				Progress Presenta	✓ Completed	Medium	Presentation ✕	
✓ Create project repository (GitHub)			5/20/2025	Initialization	✓ Completed	Medium	Research ✕	5/5
✓ Identify Research Problem				Requirement Anal	✓ Completed	Medium	Add label	3/3
✓ Supervisor & Topic Registration				Requirement Anal	✓ Completed	Medium	Add label	3/3
✓ Prepare TAF Document				Topic Assessment	✓ Completed	Medium	+1	4/4
✓ Submit TAF			6/23/2025	Topic Assessment	✓ Completed	Medium	+1	3/3
✓ Write Project Charter			7/18/2025	Project Charter	✓ Completed	Medium	+1	4/4
✓ Submit Charter Report				Project Charter	✓ Completed	Medium	+1	2/2
✓ Prepare Proposal Slides			9/5/2025	Charter Presentati	✓ Completed	Medium	Presentation ✕	4/4

+ Add new task

Q  Filters  Group by

< > March 2026  Hide future recurring tasks ☐ Week ☒ Month


Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
1 practise the presentation	2 +2 more	3 +2 more	4 +2 more	5 +2 more	6 +2 more	7 +2 more
8 +2 more	9 +2 more	10 +2 more	11 +2 more	12 ms planner submission	13 +3 more	14
15 Format according to tem...	16	17 +2 more	18	19	20	21
22	23	24	25	26	27	28
29	30 +4 more	31	1	2	3	4
5	6	7	8	9	10	11

Unscheduled tasks

+ Add task

- No label
- ☐ Add demo videos
Project Website
- ☐ Add documentation
Project Website
- ☐ Add system description
Project Website
- ☐ Create project webpage
Project Website
- ☐ Dashboard interface

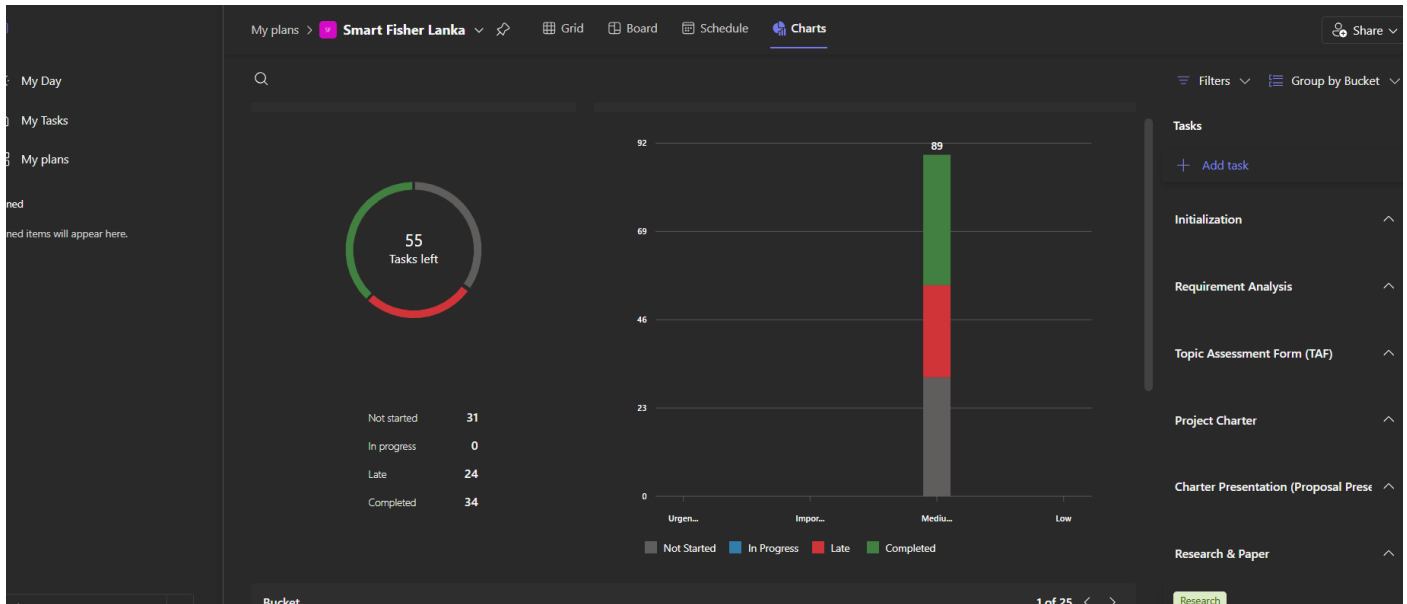Progress Monitoring



Schedule View

My plans >

Smart Fisher Lanka

Grid

Board

Schedule

Charts

Share

March 2026

Hide future recurring tasks

Week

Month

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
1 practise the pres...	2 +2 more	3 +2 more	4 +2 more	5 +2 more	6 +2 more	7 +2 more
8 +2 more	9 +2 more	10 +2 more	11 +2 more	12 ms planner subm...	13	14
15 Format according t...	16	17 +	18 +2 more	19	20	21
22	23	24	25	26	27	28
29	30	31 +4 more	1	2	3	4
5	6	7	8	9	10	11

Filters

Group by Assigned to

Unscheduled task

Group by Assigned to

+ Add task

Unassigned

Testing

Fish Quality Grading Testings

System Testing

Testing

Fish Zone Prediction Testings

System Testing

Testing

Fish Quality Grading Testings

System Testing

Testing






DATCIE Trip Cost Engine Testings

Tasks by Member

Student Number	Function
IT22215574	Fish Zone Prediction
IT22283344	Fish Quality Grading
IT22277572	DATCIE Trip Cost Engine
IT22569622	Market Price Prediction

My plans > **Smart Fisher Lanka**   Board  Schedule  Charts  Share

Q  Filters

Assignment	Start date	Due date	Bucket	Progress	Priority	Labels	Quick look
			Initialization	Completed	Medium	Add label	3/3
			Initialization	Completed	Medium	Add label	4/4
			Initialization	Completed	Medium	Add label	3/3
			Progress Presenta	Completed	Medium	Presentation	
			Progress Presenta	Completed	Medium	Presentation	
		5/20/2025	Initialization	Completed	Medium	Research	5/5
			Requirement Anal	Completed	Medium	Add label	3/3
			Requirement Anal	Completed	Medium	Add label	3/3
			Topic Assessment	Completed	Medium	+1	4/4
	6/23/2025		Topic Assessment	Completed	Medium	+1	3/3
	7/18/2025		Project Charter	Completed	Medium	+1	4/4
			Project Charter	Completed	Medium	+1	2/2
	9/5/2025		Charter Presentati	Completed	Medium	Presentation	4/4

My plans > **Smart Fisher Lanka**      Share 

 Filters 

	Assignment 	Start date 	Due date 	Bucket 	Progress 	Priority 	Labels 
Grading Testings				System Testing	☐ Not started	Medium	Testing 
Implementations	 SUMANAWEEI			Overall system de	☒ Completed	Medium	+1
Implementations	 JAYAWEERA R			Overall system de	☒ Completed	Medium	+1
Folder structure planning				Overall system de	☒ Completed	Medium	+1
Session planning meetings				Overall system de	☒ Completed	Medium	Add label
Meeting for a dataset explore and informa	   			Overall system de	☒ Completed	Medium	Field events 
NAARA for information and requirements g	  			Overall system 	☒ Completed	Medium	Field events 
PI (NestUS)	 KAUSHAN M	12/21/2025	12/30/2025	System Developm	☐ Not started	Medium	+1
PI (NestUS)	 JAYAWEERA R	12/21/2025	12/30/2025	System Developm	☐ Not started	Medium	+1
PI (NestUS)	 JAYAWEERA J I	12/25/2025	1/6/2026	System Developm	☐ Not started	Medium	+1
PI (NestUS)	 SUMANAWEEI	12/26/2025	12/31/2025	System Developm	☐ Not started	Medium	+1
Implementation	 KAUSHAN M			System Developm	☐ Not started	Medium 	+1
Implementation	 JAYAWEERA R	12/31/2025	1/4/2026	System Developm	☐ Not started	Medium	+1

References

1. Microsoft Corporation, *Microsoft Planner Documentation*, Microsoft Learn, 2024.N.
2. Microsoft Corporation, *Use Microsoft Planner to Manage Team Work*, Microsoft Support Documentation, 2024.
3. R. S. Pressman and B. R. Maxim, *Software Engineering: A Practitioner's Approach*, 8th ed., McGraw-Hill Education, 2014.
